



به نام خالق هستی
دانشگاه صنعتی امیرکبیر (پلی تکنیک تهران)
پروژه مهندسی نرم افزار ۲
مسئله‌ناقصی-رزناظری



مدیریت چرخه عمر چابک و تضمین کیفیت

پیاده‌سازی‌های اسکرام و نقاط عطف تحویل:

۱. مدیریت بک‌لاگ محصول:

Item ID	Item Name	Status	Assignee	Due Date	Priority
TIC-5	مستندات و اهداف کلان	DONE	...	3 days	High
TIC-6	تسک مستندسازی	DONE	...	3 days	High
TIC-11	Activity Diagram	DONE	...	5 days	Medium
TIC-8	use case	DONE	...	5 days	Medium
TIC-12	Component Diagram	DONE	...	5 days	Medium
TIC-10	Sequence Diagram	DONE	...	5 days	Medium
TIC-9	Class Diagram: Mapping	DONE	...	5 days	Medium
TIC-13	Deployment Diagram	DONE	...	5 days	Medium
TIC-7	بررسی نیازمندی‌های کاربردی و غیر کاربردی	DONE	...	9 days	High

Project: TicketPlus

Sprint: TIC Sprint 1

Outcome: Goal effectively met 9 of 9 committed issues were completed

This sprint established the core documentation and architecture baseline for TicketPlus. All committed work was delivered, with one item closing one day after the planned sprint end and no scope rollover into the next sprint.

Key Achievements

- Completed the full UML design set covering use case, class, sequence, activity, component, and deployment views for the platform. This created a shared technical blueprint for the ticket-booking flow, API gateway design, and Kubernetes deployment model. Key issues: [TIC-8](#), [TIC-9](#), [TIC-10](#), [TIC-11](#), [TIC-12](#), [TIC-13](#)
- Defined product goals and risk foundations early, giving the team an aligned starting point for future delivery work. Key issues: [TIC-5](#), [TIC-6](#)

Blockers and Risks

- Requirements review closed one day late. [TIC-7](#) required due-date adjustments and ownership changes before completion. The likely cause was underestimation of the analysis effort around functional and non-functional requirements, including centralized authentication considerations. Resolution: completed on . Impact: low, with no downstream scope blocked.
- Sprint closure lag created process risk. Although work finished at sprint end, the sprint was formally closed on . Resolution: administrative closure completed. Impact: risk of reduced delivery cadence and weaker sprint-to-sprint continuity.

Scope Change Summary


- Added: No new issues were added after sprint start.
- Removed: No committed issues were removed from scope.
- Carried over: No issues rolled into the next sprint. [TIC-7](#) finished slightly after the planned end date but was completed before final sprint closure.

Recommendations for Next Sprint


- Set an explicit sprint goal so progress can be measured against a clearly stated business outcome, not only issue completion.
- Break analysis-heavy work into smaller checkpoints to improve estimation accuracy and reduce the chance of due-date extensions on requirements or architecture tasks.

Key Links


- [View all sprint issues in Jira](#)
- [Referenced next sprint record](#)


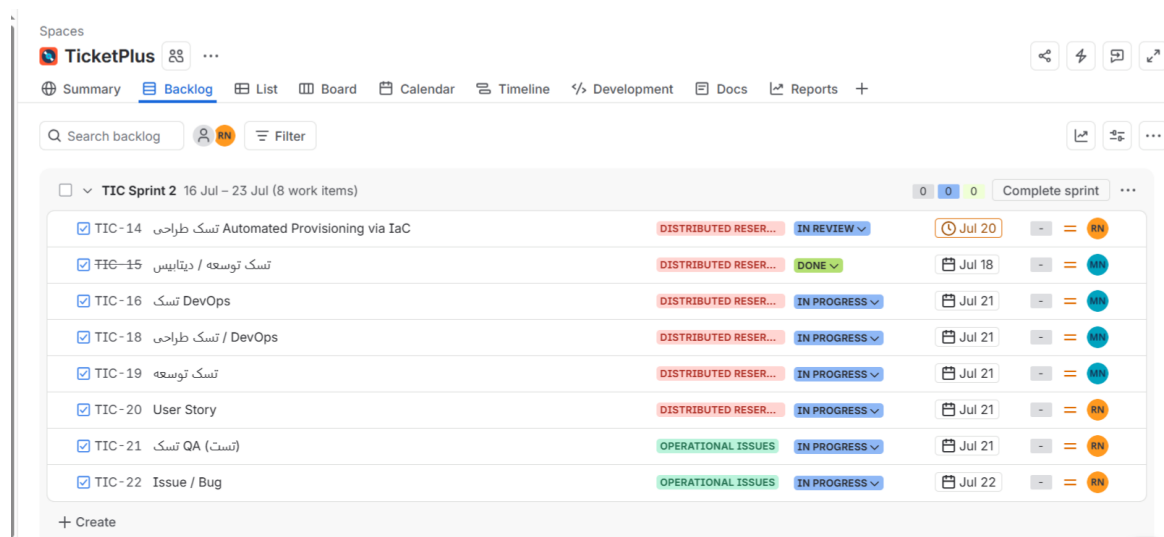


۲. اپیک‌ها و داستان‌های کاربری خرد:

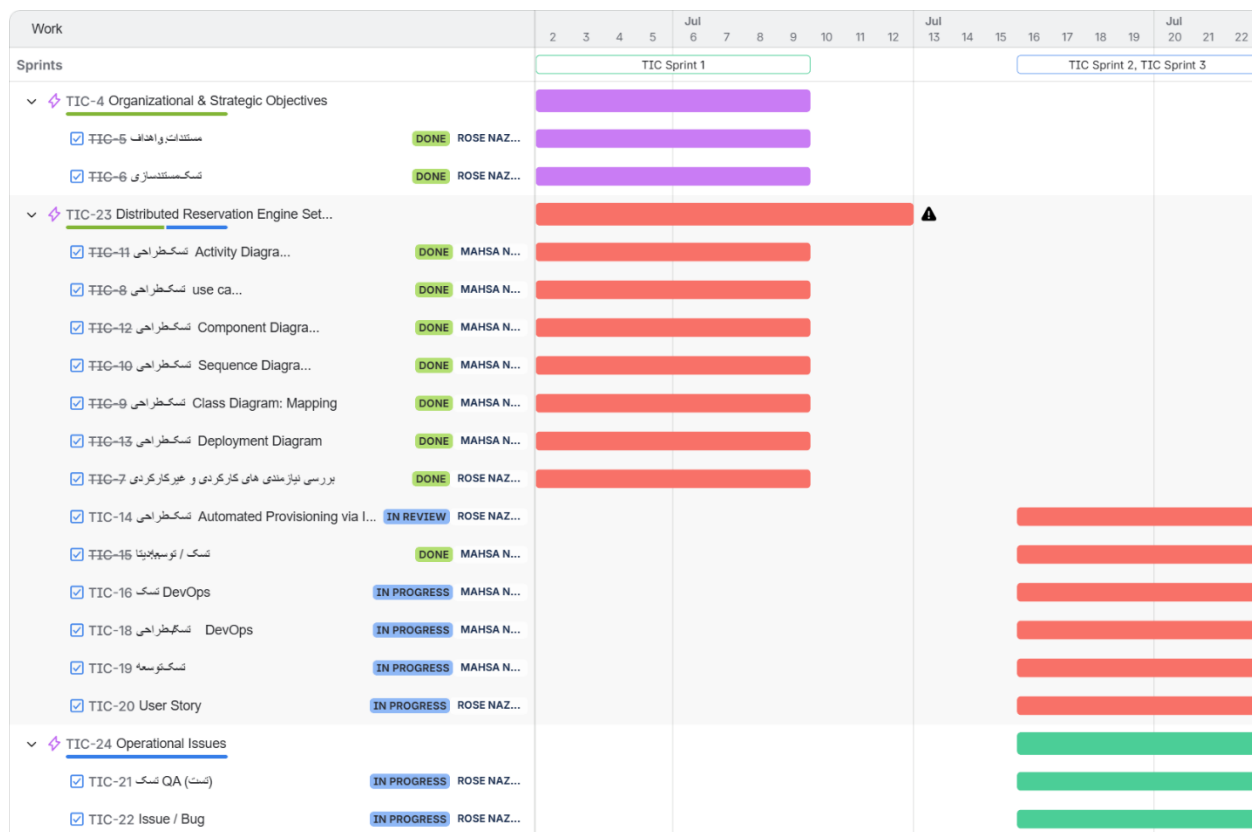

۳. برنامه‌ریزی و اجرای اسپرینت:

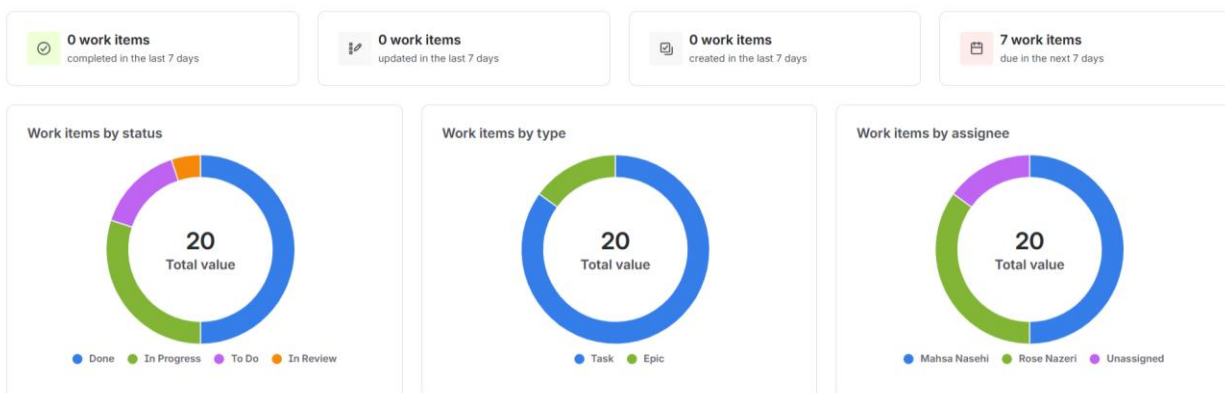

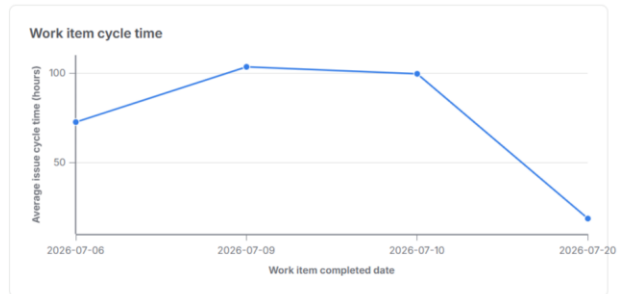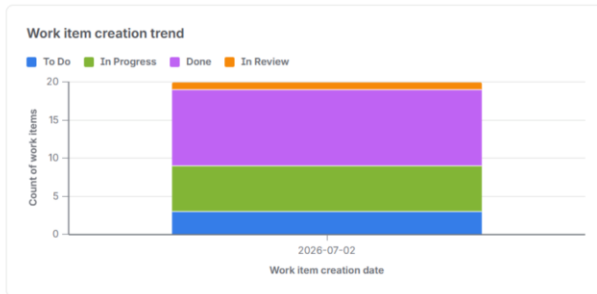

TIC-23 /
☒ TIC-14

Automated Provisioning via IaC تسک طراحی

+ ...

In Review ▾ Agents %> ⚡

✦ Improve Task

▼ **Description**

Task Description:

Develop Infrastructure as Code (IaC) to automate the deployment process (file SE_Project.pdf , page 5, line 28).

- Write declarative Terraform scripts (**Declarative Terraform scripts**).
- These scripts should be responsible for provisioning cloud instances, load balancers, and managed databases to automatically create a fully resilient environment.

TIC-23 /
☒ TIC-15

تسک توسعه / دیتابیس

+ ...

Done ▾ Agents %> ✓ Done ⚡

✦ Improve Task

▼ **Description**

Database & Access: Designing Baseline database schemas ERD Access control

Summary Backlog List **Board** Calendar Timeline Development Docs Reports

Search board Filter Group Complete sprint

To Do 0

In Progress 6

In Review 1

Test 0

Done 1

Create

Due date Jul 21, 2026

Parent Distributed Reservation Engin...

TIC-18

تسک توسعه

Due date Jul 21, 2026

Parent Distributed Reservation Engin...

TIC-19

User Story


Due date Jul 21, 2026

تسک توسعه / دیتابیس

Due date Jul 18, 2026

Parent Distributed Reservation E

TIC-15

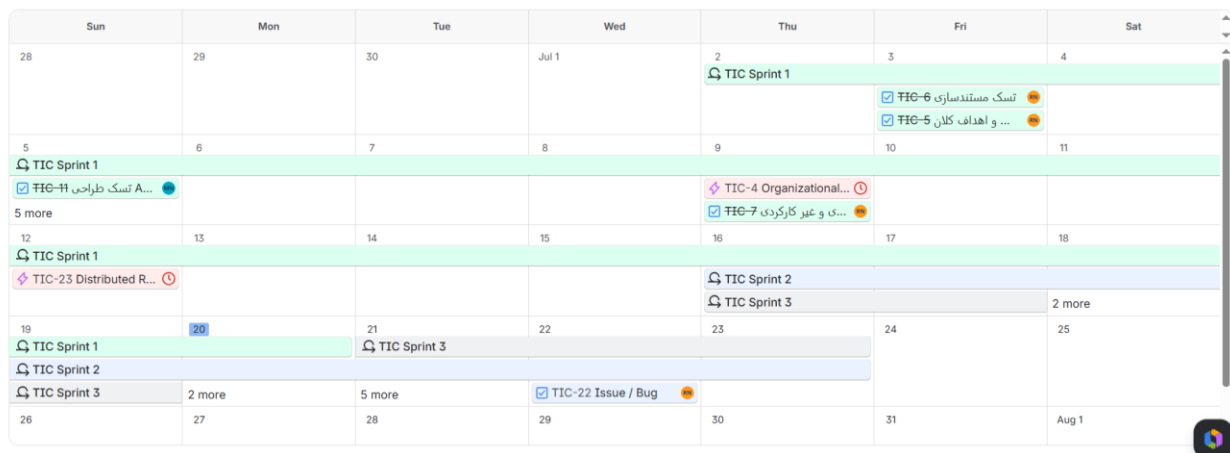

دسترسی space جیرا رو باز کردیم :

<https://rosenazeri83.atlassian.net/jira/software/projects/TIC/boards/37/calendar?atlOrigin=eyJpIjoiZjc0YzZmNTMzNTM3NGU2MGI2N2U5YjRkYTQ5YzQ5MjgiLCJwIjoiajI9>
