




به نام خالق هستی  
دانشگاه صنعتی امیرکبیر (پلی تکنیک تهران)  
پروژه مهندسی نرم افزار ۲  
مسانا صبحی - رزنا نظری



مدیریت چرخه عمر چابک و تضمین کیفیت پیاده‌سازیهای اسکرام و نقاط عطف تحویل:

۱. مدیریت بکلاگ محصول:

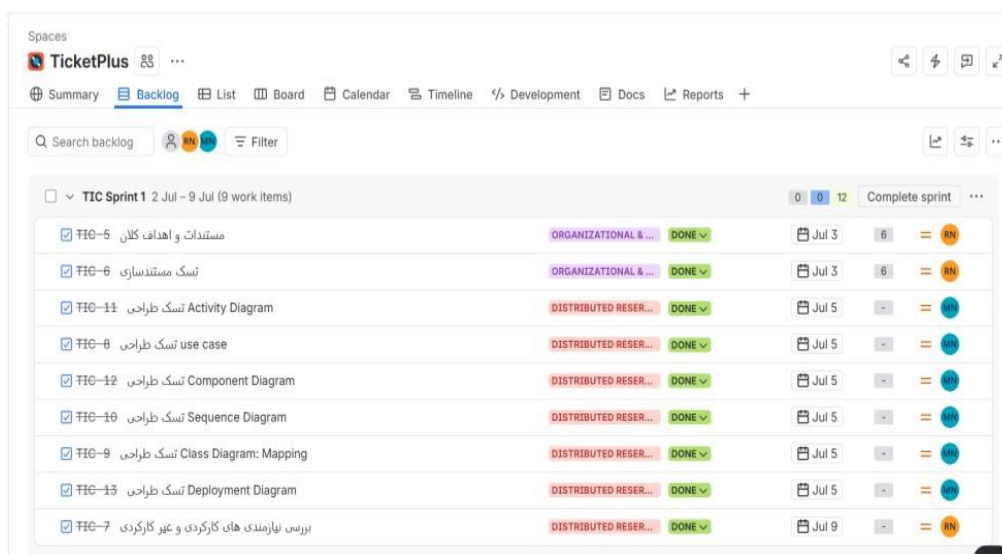

Sprint: TIC Sprint 1

Outcome: Goal effectively met 9 of 9 committed issues were completed

This sprint established the core documentation and architecture baseline for TicketPlus. All committed work was delivered, with one item closing one day after the planned sprint end and no scope rollover into the next sprint.

Key Achievements

- Completed the full UML design set covering use case, class, sequence, activity, component, and deployment views for the platform. This created a shared technical blueprint for the ticket-booking flow, API gateway design, and Kubernetes deployment model. Key issues: [TIC8](#), [TIC-9](#), [TIC-10](#), [TIC-11](#), [TIC-12](#), [TIC-13](#)

- Defined product goals and risk foundations early, giving the team an aligned starting point for future delivery work. Key issues: [TIC-5](#), [TIC-6](#)

### Blockers and Risks

- Requirements review closed one day late. [TIC-7](#) required due-date adjustments and ownership changes before completion. The likely cause was underestimation of the analysis effort around functional and non-functional requirements, including centralized authentication considerations. Resolution: completed on . Impact: low, with no downstream scope blocked.
- Sprint closure lag created process risk. Although work finished at sprint end, the sprint was formally closed on . Resolution: administrative closure completed. Impact: risk of reduced delivery cadence and weaker sprint-to-sprint continuity.

### Scope Change Summary


- Added: No new issues were added after sprint start.
- Removed: No committed issues were removed from scope.
- Carried over: No issues rolled into the next sprint. [TIC-7](#) finished slightly after the planned end date but was completed before final sprint closure.

### Recommendations for Next Sprint

- Set an explicit sprint goal so progress can be measured against a clearly stated business outcome, not only issue completion.
- Break analysis-heavy work into smaller checkpoints to improve estimation accuracy and reduce the chance of due-date extensions on requirements or architecture tasks.


### Key Links

- [View all sprint issues in Jira](#)
- [Referenced next sprint record](#)

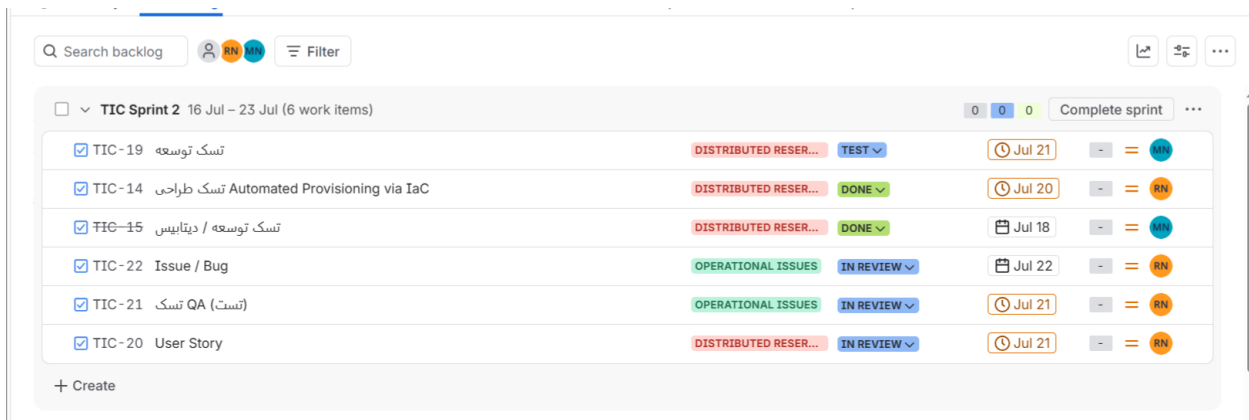

| Issue ID | Issue Name                     | Status               | Priority  | Due Date | Assignee |
|----------|--------------------------------|----------------------|-----------|----------|----------|
| TIC-19   | تسک توسعه                      | DISTRIBUTED RESER... | TEST      | Jul 21   | RN       |
| TIC-14   | Automated Provisioning via IaC | DISTRIBUTED RESER... | DONE      | Jul 20   | RN       |
| TIC-15   | تسک توسعه / دیتابیس            | DISTRIBUTED RESER... | DONE      | Jul 18   | RN       |
| TIC-22   | Issue / Bug                    | OPERATIONAL ISSUES   | IN REVIEW | Jul 22   | RN       |
| TIC-21   | تسک QA (تست)                   | OPERATIONAL ISSUES   | IN REVIEW | Jul 21   | RN       |
| TIC-20   | User Story                     | DISTRIBUTED RESER... | IN REVIEW | Jul 21   | RN       |



## ۲. اپیک ها و داستانهای کاربری خرد:

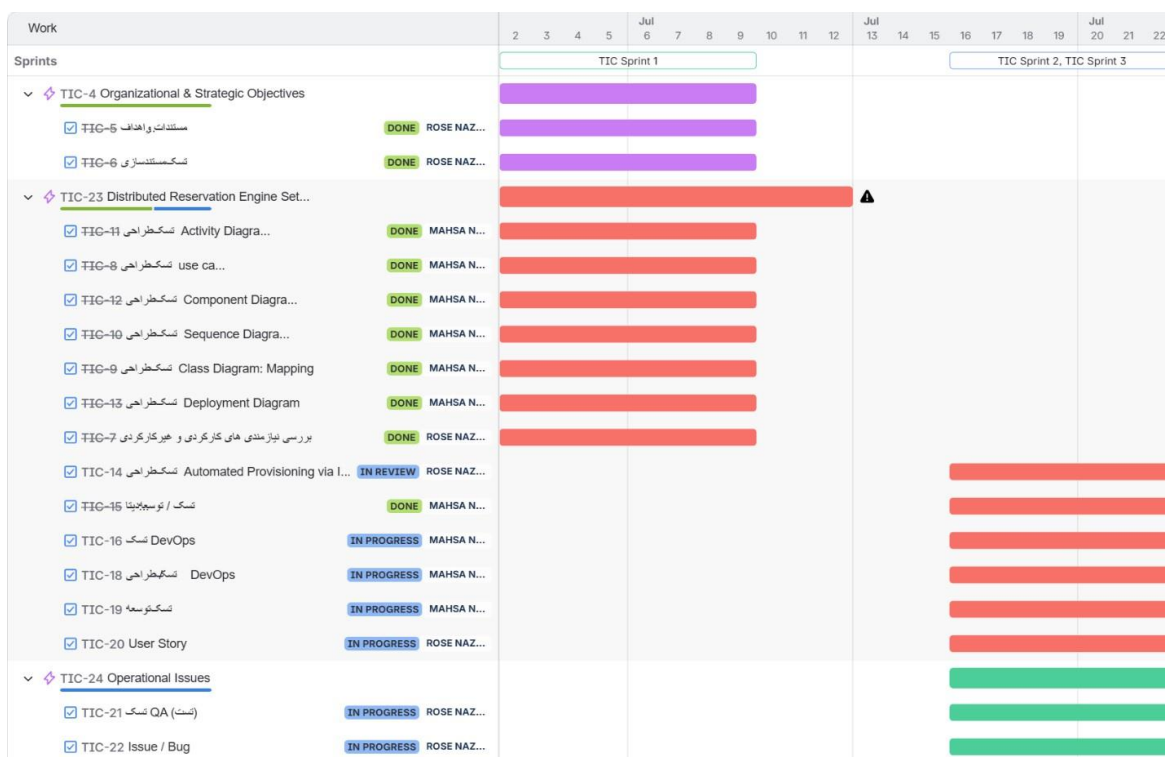

| ردیف | Epic                                  | Sprint | نوع آیتم / Task      | شرح                                                                                                               |
|------|---------------------------------------|--------|----------------------|-------------------------------------------------------------------------------------------------------------------|
| ۱    | Strategic & Organizational Objectives | -      | مستندات و اهداف کلان | Key Product Goals: تجربه کاربری یکپارچه (Seamless UX). اعتمادسازی پلتفرم (Reliability) & Trust.                   |
| ۲    | Strategic & Organizational Objectives | -      | تسک مستندسازی        | Required System Documentation: تدوین سند Risk Mitigation برای تحلیل نقاط شکست و ترافیک ناگهانی.                   |
| ۳    | Reservation Distributed Engine Setup  | ۱      | تسک فنی              | Functional Specs: پیاده سازی سیستم احراز هویت متمرکز (Centralized Identity) با JWT یا OAuth2.                     |
| ۴    | Reservation Distributed Engine Setup  | ۱      | تسک طراحی (UML)      | Sequence & Use Case, Class Diagram: طراحی جریان رزرو، موجودیت های اصلی (Event, Ticket, Venue) و جریان End-to-End. |

|    |                                               |              |                     |                                                                                                                 |
|----|-----------------------------------------------|--------------|---------------------|-----------------------------------------------------------------------------------------------------------------|
| ۵  | Reservation Distributed Engine Setup          | ۱            | تسک طراحی (UML)     | Component Diagram: تعیین مرزهای عملیاتی، دامنه‌های بیزینسی و ادمین پنل.                                         |
| ۶  | Reservation Distributed Engine Setup          | ۱            | تسک توسعه / دیتابیس | Access & Database: طراحی و Baseline database schemas کنترل دسترسی‌ها.                                           |
| ۷  | Reservation Distributed Engine Setup          | ۱            | تسک DevOps          | CI/CD Pipelines: راه‌اندازی GitLab CI/CD و الزامات Unit test روی هر کامیت.                                      |
| ۸  | Reservation Distributed Engine Setup          | ۱            | تسک توسعه           | Reports & UI: راه‌اندازی Layout builders و پنل‌های گزارش‌گیری.                                                  |
| ۹  | Reservation Distributed Engine Setup          | ۲            | تسک طراحی (UML)     | Activity Diagram: مدل‌سازی مسیر خرید کاربر (Purchase Journey) و حالت‌های رول‌بک.                                |
| ۱۰ | Reservation Distributed Engine Setup          | ۲            | تسک طراحی / DevOps  | Deployment Diagram: طراحی ساختار استقرار مبتنی بر Kubernetes و API Gateway برای Auto-scaling.                   |
| ۱۱ | Reservation Distributed Engine Setup          | ۲            | تسک توسعه           | Integration & Logic: توسعه Queue workers و یکپارچه‌سازی درگاه‌های پرداخت.                                       |
| ۱۲ | Reservation Distributed Engine Setup          | ۲            | Story User          | Seat Locking: پیاده‌سازی منطق قفل شدن صندلی به مدت ۱۰ دقیقه در زمان پرداخت.                                     |
| ۱۳ | Reservation Distributed Engine Setup          | ۲            | تسک QA (تست)        | Assurance Quality: انجام Load/Stress Testing, Mutation Testing و بررسی Code coverage.                           |
| ۱۴ | Epic (جداگانه برای باگ‌ها) Operational Issues | در طول پروژه | Bug / Issue         | Production Issues: مدیریت مشکلات احتمالی مثل خطای همزمانی (Overbooking)، قطعی درگاه، قطعی پرداخت و تایم‌اوت‌ها. |

### ۳. برنامه‌ریزی و اجرای اسپرینت:

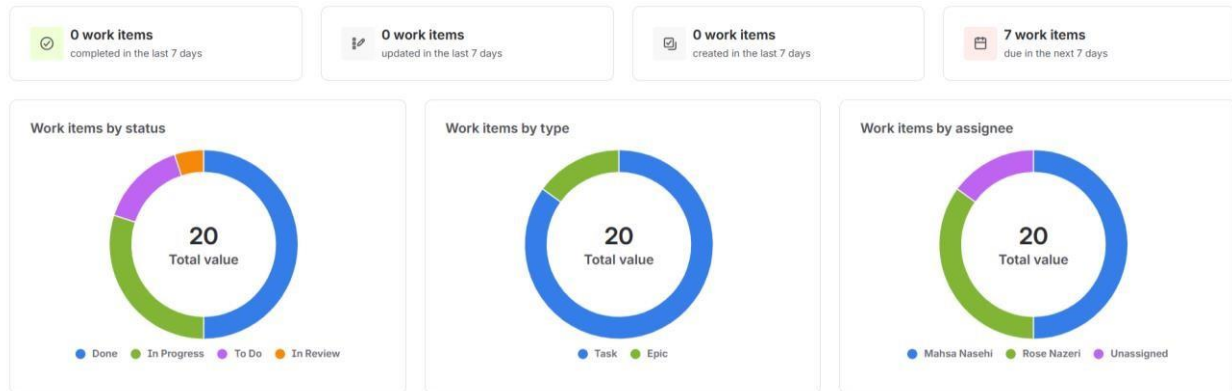

TIC-23 /

TIC-14

Automated تسک طراحی Provisioning via IaC

In Review

Agents

%

⚡

Improve Task

Description

Task Description:

Develop Infrastructure as Code (IaC) to automate the deployment process (file SE\_Project.pdf, page 5, line 28).

- Write declarative Terraform scripts (Declarative Terraform scripts).
- These scripts should be responsible for provisioning cloud instances, load balancers, and managed databases to automatically create a fully resilient environment.

TIC-23 /

TIC-15

تسک توسعه / دیتابیس

Done

Agents

%

✓ Done

Improve Task

Description

Database & Access: Designing Baseline database schemas ERD Access control

Summary Backlog List **Board** Calendar Timeline Development Docs Reports

Search board Filter Group Complete sprint

To Do 0  
+ Create

In Progress 6

In Review 1

Test 0

Done 1

تسک توسعه / دیپتایس  
Due date: Jul 18, 2026  
Parent: Distributed Reservation E  
TIC-15

تسک توسعه  
Due date: Jul 21, 2026  
Parent: Distributed Reservation Engin...  
TIC-19

تسک طراحی Automated Provisioning via IaC  
Due date: Jul 20, 2026  
Parent: Distributed Reservation Engine S...  
TIC-14

User Story  
Due date: Jul 21, 2026  
Parent: Distributed Reservation Engin...  
TIC-18



لینک عمومی جیرا:

<https://rosenazeri83.atlassian.net/jira/software/projects/TIC/boards/37/calendar?atlOrigin=eyJpIjoiZjc0YzMzNTMzNTM3NGU2MGU2MGI2N2U5YjRkYTQ5YzQ5MjgiLCJwIjoiaWJ9>
